

# PHOTO REPORT

Reconstruction of the Dormitory, Irpin

May – June, 2023



ЖИТЛО  
ДЛЯ ВПО

# May 10-20, 2023


Connecting to city utilities. Water and electricity.



ЖИТЛО  
ДЛЯ ВПО

# May 24-25, 2023

Fencing the perimeter of the site.  
Construction site arrangement

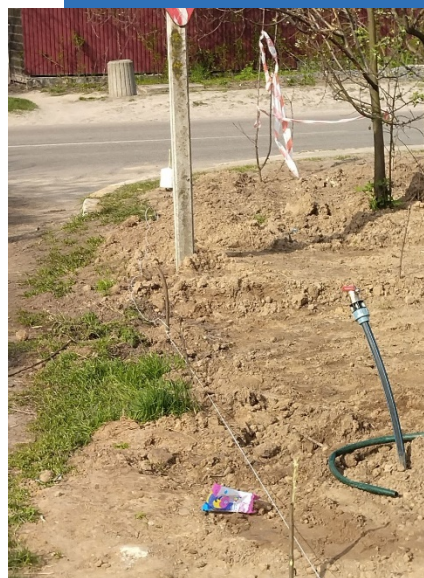

ЖИТЛО  
ДЛЯ ВПО

# June 1-3, 2023

Installation of the fencing and security at the construction site



ЖИТЛО  
ДЛЯ ВПО

# June 5-8, 2023

Completing the fence and entrance gates.  
The dismantling of wooden windows  
and doors has begun.



ЖИТЛО  
ДЛЯ ВПО

# June 6-12, 2023

Dismantling the 0 level.



ЖИТЛО  
ДЛЯ ВПО

# June 16, 2023

Delivery of construction materials: sand, cement and bricks for filling holes and aligning windows openings



ЖИТЛО  
ДЛЯ ВПО

# June 15-20, 2023

Dismantling the 1 level.



ЖИТЛО  
ДЛЯ ВПО



# June 20, 2023

Construction garbage disposal. 7 trucks, each with 20 m3 of load  
Dismantling works



ЖИТЛО  
ДЛЯ ВПО

# June 20-23, 2023

Cutting out openings for windows, strobes for reinforcing lintels, floors for the construction of foundations for walls and partitions, dismantling plaster



ЖИТЛО  
ДЛЯ ВПО
